DESTRUCTION
CAWARDEN
TO
CONSTRUCTION

Turnpike Close, Grantham

Site Clearance and Enabling Works

ID	Name	Start	Duration	Finish
1	**Enabling Works**	19/09/22	0d	19/09/22
2	Prepare RAMS & CPP	19/09/22	10d	30/09/22
3	Review Service Disconnections	03/10/22	10d	14/10/22
4	Site Managers Inductions	14/10/22	1d	14/10/22
5	Install Noise, Dust and Vibration Monitoring	17/10/22	1d	17/10/22
6				
7	**On Site Works**			
8	Set Up Site	17/10/22	4d	20/10/22
9	Install Site Fencing including tree protection	17/10/22	5d	21/10/22
10	Investigate/uncover AWA SW & Foul Manholes as required for CCTV team	19/10/22	3d	21/10/22
11	Install 3m stand off from retained drainage	17/10/22	3d	19/10/22
12	Clear existing site vegetations	19/10/22	6d	26/10/22
13	Break/grub up existing floor slab and foundations	24/10/22	35d	09/12/22
14	Cap existing drainage as required	21/11/22	1d	21/11/22
15	Crush hard-core to 6f2 and stockpile for re use	14/11/22	30d	23/12/22
16	Raise tarmac hard standings and crush (if required)	05/12/22	10d	16/12/22
17	DECAMP	23/12/22	0d	23/12/22
18	PREPARE H&S FILE	26/12/22	10d	06/01/23
19				

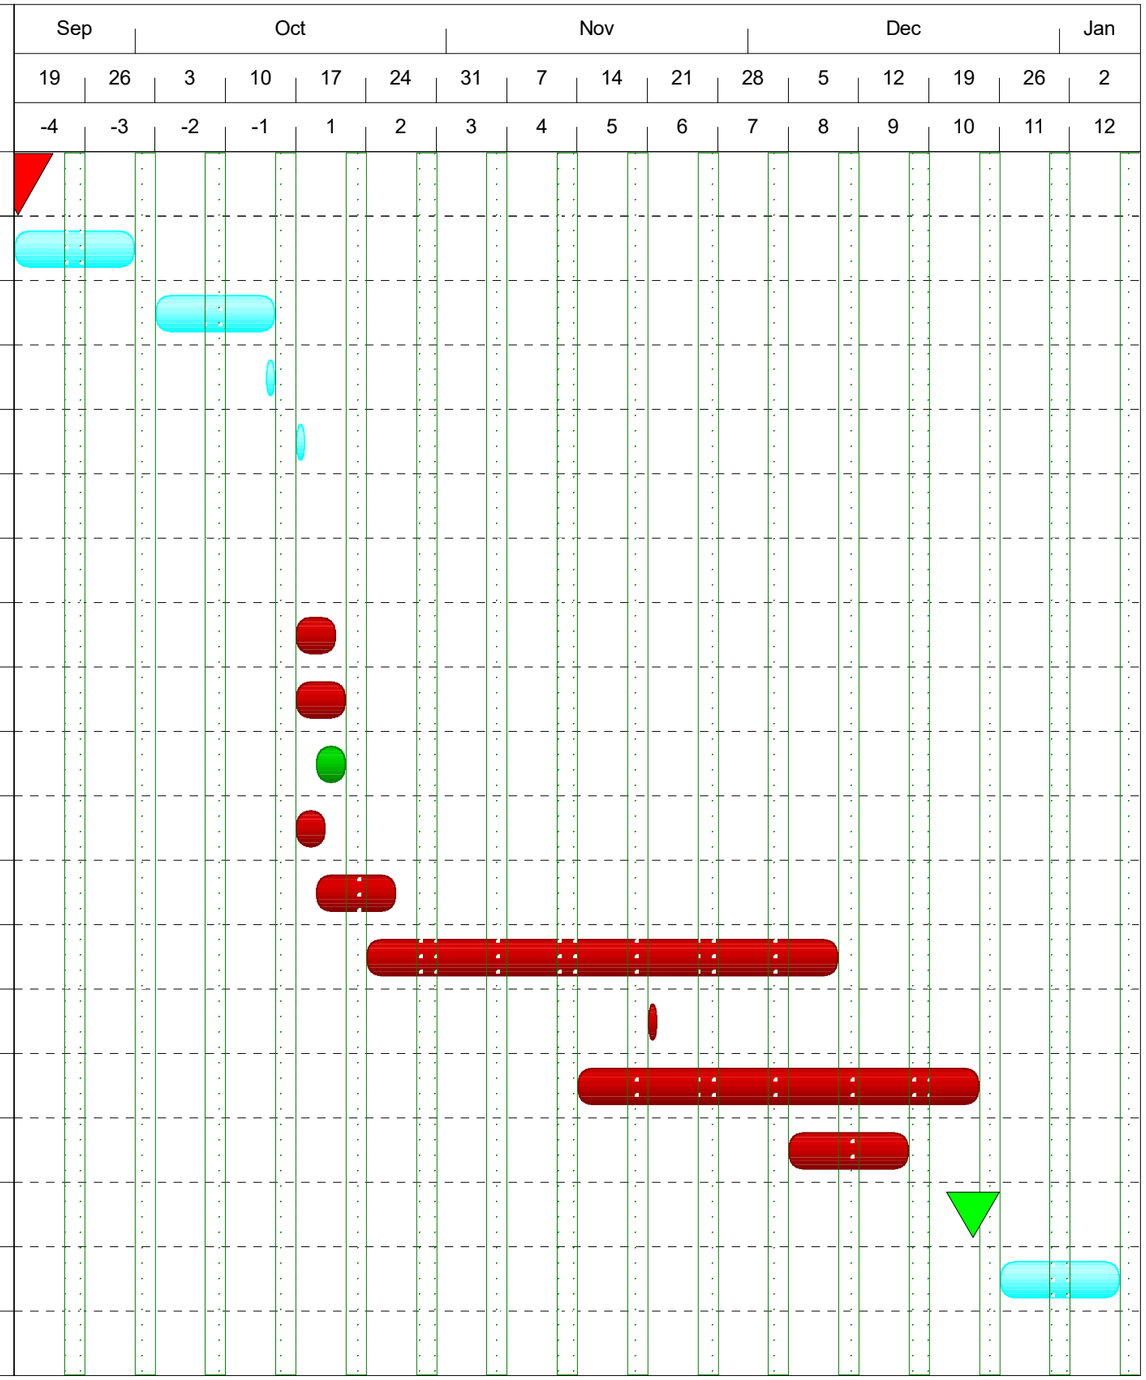

Completion | Main Demolition | Instruction | Post Demolition Works | Investigation Works | Enabling Works
